


Student Success District Bear Down Gym Preservation & Renovation

Construction Update - Week of July 19, 2021



Inside the main entrance standing on the historic gym floor, looking south. Level 3 bathrooms are getting tile! Level 2 is getting paint, and level 1 is getting framed and drywalled!

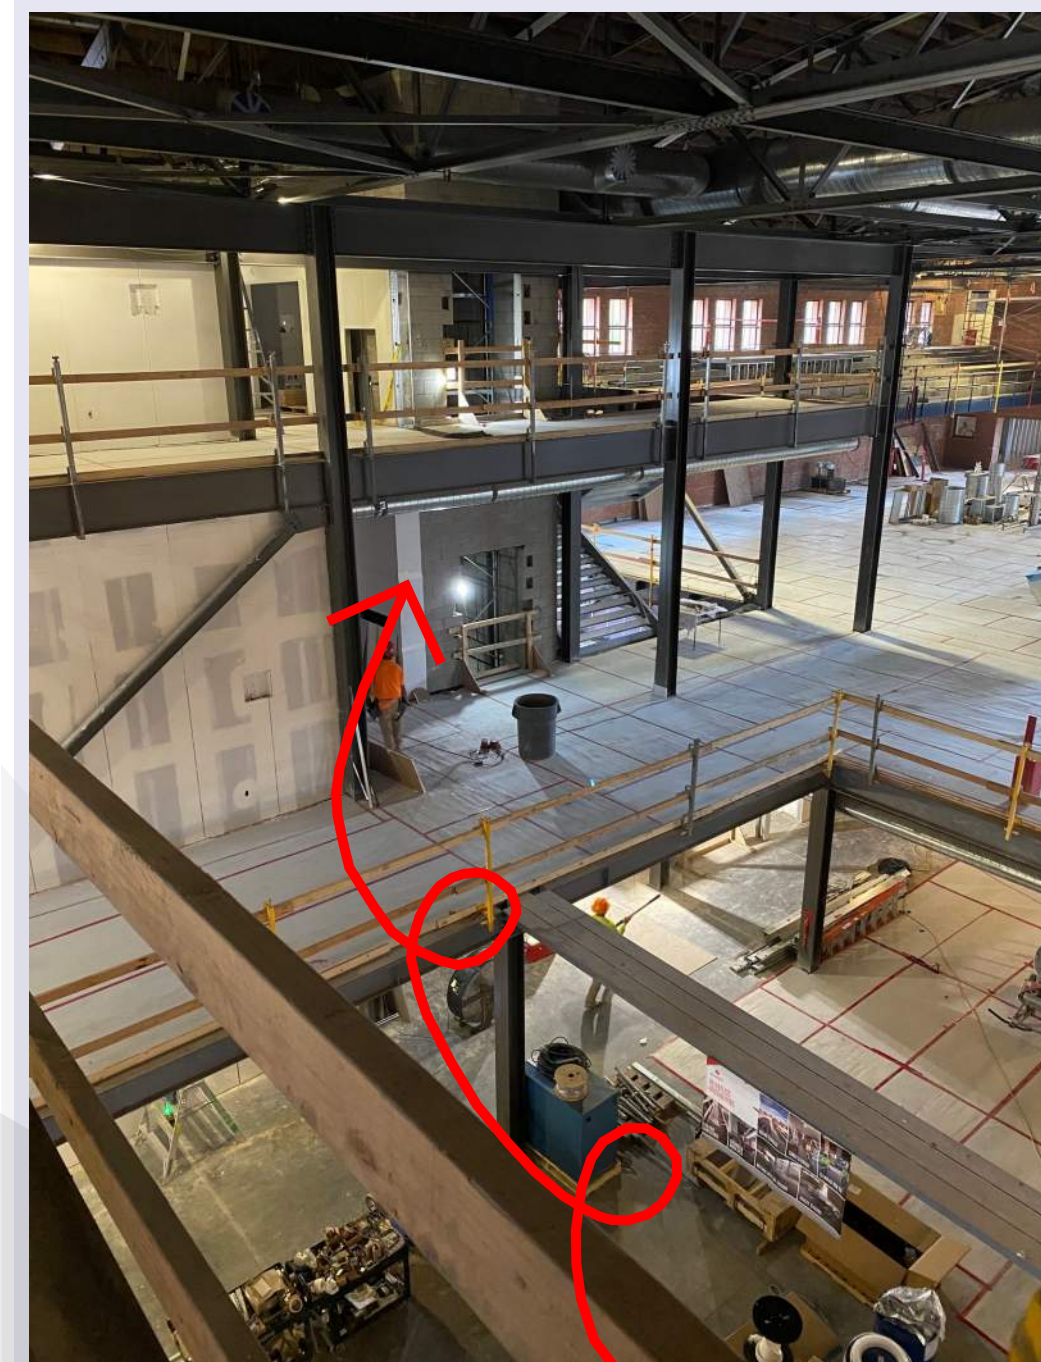


On the left, the elevator crew has a scaffold inside the elevator shaft running all the way from the pit in level 1 to barrel roof ceiling above level 3! On the right, window frames are ready for glass installation in the southern opening. Once the windows are installed the building will be ready for air conditioning!



Student Success District Bear Down Gym Preservation & Renovation

Construction Update - Week of July 19, 2021

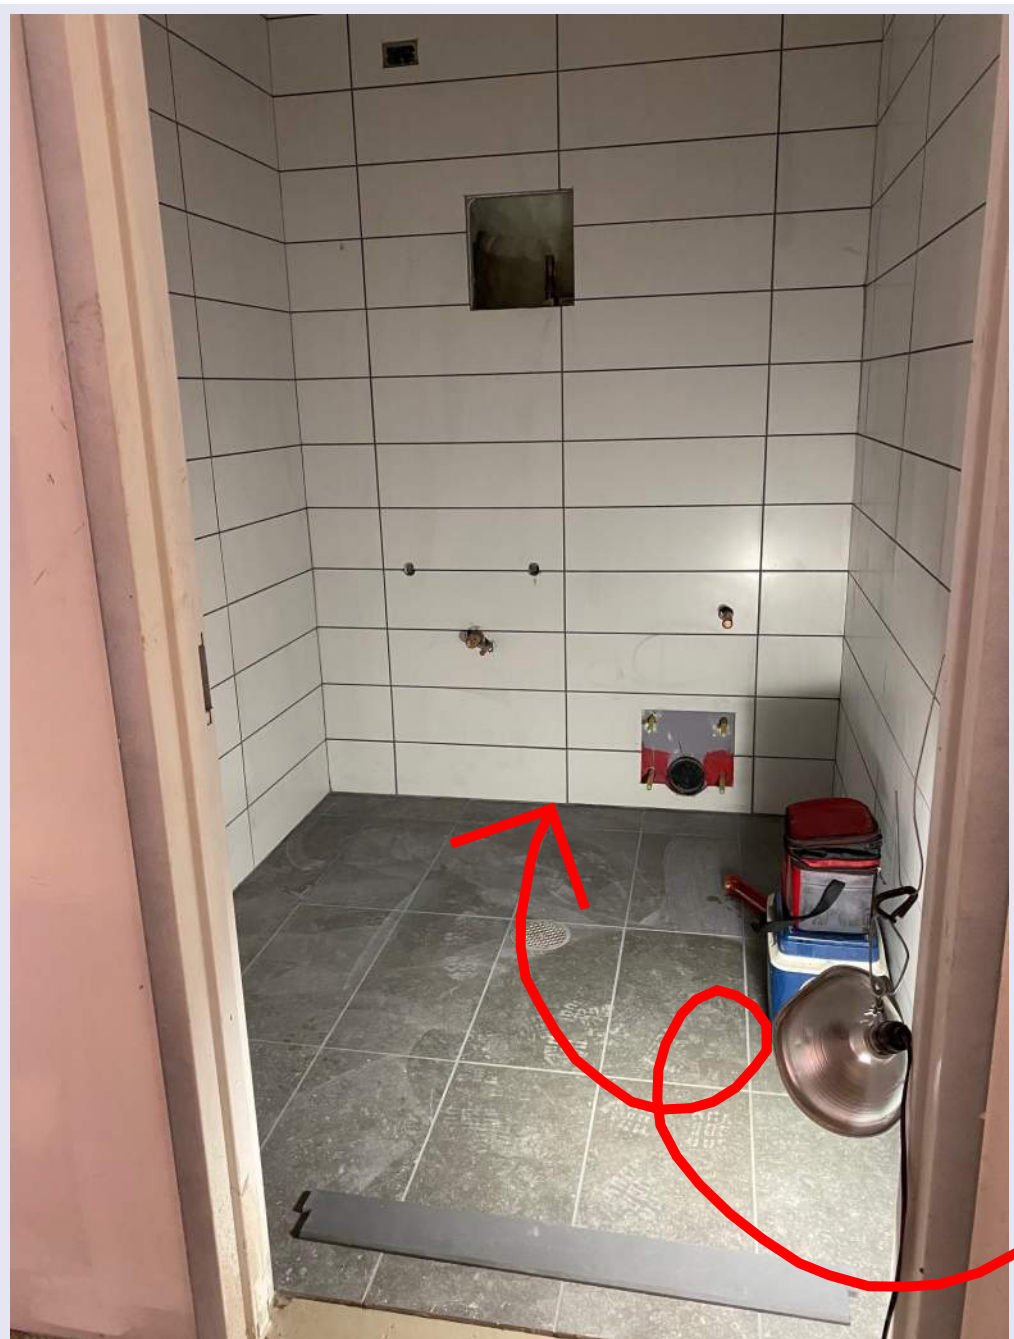

On the left, tile is installed in one of eight level 3 bathrooms! On the right, the replacement for the bike path has begun off of E 4th St. and N Highland Ave.

The meeting rooms on level 3 are getting painted. Each room will have an accent color on one side to match the theme in the Main Library and the Bartlett Academic Success Center! Check it out!

